

तत् त्वं पूषन् अपावृषु
केन्द्रीय विद्यालय संगठन

DETAILED PROJECT REPORT

For Seeking loan from HEFA

KENDRIYA VIDYALAYA SANGATHAN

18, Institutional Area, Shaheed Jeet Singh Marg,


New Delhi-110016 Phone : 011-26965154

E-mail : kvs.commissioner@gmail.com

www.kvsangathan.nic.in

**DETAILED PROJECT REPORT (DPR) ON CONSTRUCTION OF
SCHOOL BUILDINGS OF KENDRIYA VIDYALAYAS**

S.No.	CONTENT	PAGE
1.	INTRODUCTION	2
2	PROCEDURE FOR OPENING OF KENDRIYA VIDYALAYAS	5
3	SALIENT FEATURES OF THE SCHEME	7
4	SYSTEM & PROCEDURE OF EXECUTION OF WORKS	11
5.	ESTIMATION / PROJECT COST / FUNDING PATTERN OF SCHEME	15
6.	COMPONENTS OF THE SCHEME	20
7.	SCHEDULE OF IMPLEMENTATION	20
8.	BUDGET REQUIREMENT & ALLOCATION	21
9.	CONCLUSION	25
10.	PHOTOGRAPHS OF COMPLETED SCHOOL BUILDINGS (ANNEXURE III)	43


 संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (विन)/Assistant Commissioner (Fin)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, संस्थागत क्षेत्र 18, Institutional Area
 शहीद जेत सिंह मार्ग/Shahed Jeet Singh Marg
 नई दिल्ली-110 016/New Delhi-110 016

INTRODUCTION

The Scheme of Central Schools was approved in November 1962 by the Govt. of India on the recommendations of the Second Central Pay Commission in which it was recommended that the Government should develop a scheme to provide uninterrupted education to the wards of transferable Central Government employees. Consequently, Central School Organization was started as a unit of the Ministry of Education (Now Ministry of Human Resource Development) of the Govt. of India.

Initially, 20 Regimental schools were adopted, which were functioning at places having large concentration of defence personnel as Central Schools during the academic year 1963-64.

The Kendriya Vidyalaya Sangathan (KVS) was registered as a society under the Societies Registration Act (XXI of 1860) on 15th December 1965. The primary aim of the Sangathan is to provide, establish, endow, maintain, control and manage the Central Schools (Kendriya Vidyalayas) located all over India and abroad.

KVS is an autonomous body under MHRD fully financed by the Government. Over the years, the number of Kendriya Vidyalayas steadily increased to 1183 as on 01.05.2018.




संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, संस्थान क्षेत्र/18, Institutional Area
 शहीद जगत सिंह मार्ग/Shahid Jeet Singh Marg
 नई दिल्ली-110 016/New Delhi-110 016

OBJECTIVES

- (a) To cater to the educational needs of the children of transferable Central Government employees including Defence and Para-military personnel by providing a common education programme.
- (b) To pursue excellence and set the pace in the field of school education.
- (c) To initiate and promote experimentation and innovations in education in collaboration with other bodies like the Central Board of Secondary Education (CBSE) and the National Council of Educational Research and Training (NCERT) etc.
- (d) To develop the spirit of national integration and create a sense of "Indianness" among children.

In pursuance of the above objectives, the Kendriya Vidyalayas have the following features and norms:

- Common textbooks and bilingual (English & Hindi) medium of instruction.
- All Kendriya Vidyalayas are affiliated to Central Board of Secondary Education (CBSE).
- All Kendriya Vidyalayas are co-educational composite schools.
- Teaching of three languages – English, Hindi & Sanskrit from Class VI to VIII is compulsory. In Classes IX and X, any two languages out of English, Hindi and Sanskrit can be opted. Sanskrit can also be taken as an elective subject at + 2 stages.
- Through an ideal and updated methodology, KVS strives to maintain excellence in academic pursuits.


 संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वि.)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संस्थान/Kendriya Vidyalaya Sangathan
 18, संस्थान क्षेत्र/18, Institutional Area
 शहीद जगत सिंह मार्ग/Shahid Jagan Singh Marg
 नई दिल्ली-110 016/New Delhi-110 016

ADMINISTRATION

(a) Sangathan has 03 tier Management Structure

- Headquarter at New Delhi.
- 25 Regional Offices, to manage schools put under their Administrative Control.
- Kendriya Vidyalayas, spread all over the country & abroad.

(b) Functioning of KVS

- KVS has its General Body called Sangathan comprising of 31 Members.
- The Board of Governors has 25 Members.
- 04 Standing Committees constituted to assist the BoG i.e. Academic Advisory Committee, Finance Committee, Works Committee and Establishment & Administration Committee.

The Minister for Human Resource Development is ex-officio Chairman of the Sangathan. The policy and guidelines issued by the Sangathan and its Board of Governors are executed by the Commissioner who is the Executive Head of the Sangathan.

ESTABLISHMENT

Sanctioned posts of Teaching /Non-teaching

Staff as on 31.03.2018	:	58312
Staff in Position as on 31.03.2018	:	45694
Vacancy Position as on 31.03.2018	:	12618


संजय कुमार / SANJAY KUMAR

सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
18 संस्थान क्षेत्र/18 Institutional Area
शहीद जवाहर लाल नेहरू मार्ग, शाहीद जवाहर लाल नेहरू मार्ग
नई दिल्ली-110 016/New Delhi-110 016

Sl. No.	Category	Sanctioned Posts	In Position	Vacancies
1.	Non-teaching Staff	11533	6987	4546
2.	Teaching	46779	38707	8072
	Total	58312	45694	12618

ACADEMIC PERFORMANCE

The board examination result of the Kendriya Vidyalayas has been much better than the average result of CBSE affiliated schools which are indicated as under:-


Class -X

Class-XII

Year	KVS	CBSE	KVS	CBSE
2013	99.90%	98.76%	94.82%	82.10%
2014	99.59%	98.87%	97.39%	82.66%
2015	99.39%	97.32%	94.75%	82.00%
2016	98.92%	96.21	95.43%	83.05%
2017	99.73%	90.95%	95.86%	82.02%

2. PROCEDURE OF OPENING OF KENDRIYA VIDYALAYAS

Kendriya Vidyalayas are opened on receipt of proposal from Sponsoring Authorities, viz (a) Ministry (b) Department of Govt. of India (c) State Governments (d) UTs, on the conditions that required suitable land as per KVS norms is provided free of cost on lease / permanent grant basis and also the temporary accommodation is provided to run the Vidyalaya till KVS constructs


 संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, सरयागत रोड, इन्दौर, मध्य प्रदेश
 जीत सिंह मार्ग/Chalced Jait Singh Marg
 New Delhi-110 016

its own school building on the land provided. Prior to 2014, Kendriya Vidyalayas were opened on the assurance that the Sponsoring Authority will provide land and proper physical infrastructure to run the Vidyalaya. However from the year 2014, the criteria for opening of Kendriya Vidyalayas have been changed. The present provision includes transfer of land prior to opening of a Kendriya Vidyalaya and provide temporary accommodation and to handover the possession prior to opening of new KV. The requisite extent of land to be provided free of cost is as under:

S.No.	LOCATION	Minimum Extent of Land (In Acres)	Desirable Extent of Land (In Acres)
1.	Metropolitan cities and Hyderabad & Bangalore (also including LWE affected Districts, States of Jammu and Kashmir, Himachal Pradesh, Utrakhand, North Eastern States including Sikkim)	2.5	5.00
2.	All other Locations.	5.00	10.00

The sponsoring authority should provide desirable extent of land for creation of all sports and other infrastructural facilities and for future expansion of KV. Water and electricity lines/ supply and approach road up to the site offered by sponsoring authority for construction of permanent school building will also be provided by the sponsoring authorities at their cost.

Essential Factors for considering land suitability:

- Road connectivity to the offered plot.
- Low lying and undulated plot should be avoided to minimize the development cost.



संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, शाहीद जहाँ सिद्धू मार्ग, शानेद जे. सी. मार्ग
 नई दिल्ली-110 016/New Delhi-110 016

- Availability of water supply up to site.
- Availability of Electrical connection up to site.
- Plot having HT line will not be considered.
- Land having LT line, nallah / drain passing the plot, will be avoided.
- Preference to be given to rectangular plots.
- Land should be free from encroachment and Court cases.


It is to endeavor of the KVS to construct permanent school building for all the functional Kendriya Vidyalayas in the least possible time for the benefit of the children to have conducive environment required for teaching learning process.

3. SALIENT FEATURES OF SCHEME

As per the terms and conditions accepted prior to opening of Kendriya Vidyalaya, Sponsoring Authorities will provide adequate suitable land free of cost and safe temporary building for running of Vidyalaya till KVS constructs its own permanent school building.

(a) Procedure for transfer of land:

- In respect of Kendriya Vidyalayas sponsored by the Ministry of Defence, Sanction Order for transfer of free of cost Defence land on 99 years' lease basis is issued by the Ministry of Defence.
- For Kendriya Vidyalayas located in Para-Military Stations (CRPF, BSF, ITBP, CISF, Assam Rifles etc.), Sanction Order for transfer of land is issued by the Directorate General of the concerned posts under Ministry of Home Affairs for 99 years' lease basis.
- For Kendriya Vidyalayas located in Railway Establishments, Sanction Order for transfer of land is issued by the General Manager of concerned Railway with the concurrence of Railway Board for 99 years' lease basis.




संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, सशान्त क्षेत्र 18, Institutional Area
 शहीद जीत सिंह मार्ग/Shahed Jeel Singh Marg
 110 016/New Delhi-110 016

- In respect of Civil Sector Kendriya Vidyalayas, Sponsored by the State/UT Government, the land is provided either on lease basis or on permanent grant basis (i.e. change of title in favour of KVS) and Sanction Order of State Govt. /UT for transfer of land is issued by the District Collector or the authority to whom the powers have been delegated by the State Government.
- From KVS side, Additional Commissioner (Admn) is the Competent Authority to sign the lease deed on behalf of KVS in view of the provisions laid down in the Memorandum of Associations of KVS.
- The lease documents prepared on the basis of Standing Lease Agreement duly vetted by the concerned Ministry is sent to KVS (HQ). After the signatures of the Additional Commissioner (Admn), the lease deed is registered in the Local Revenue Office.
- Lease deed is not required wherever land is transferred by the State government / UTs on permanent grant basis.


(b) Status of Kendriya Vidyalaya School Buildings as on 01.05.2018

(1)	Total Number of Kendriya Vidyalayas	1183
(2)	In Project Sector (108) / IHL (33) / Abroad (03) for which sponsoring authority provide school building as per terms and conditions	(-) 144
(3)	Other / Remaining Kendriya Vidyalayas	1039
(4)	Kendriya Vidyalayas with Permanent Building	775


 संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, संस्थागत क्षेत्र/18, Institutional Area
 शाहीद जैत सिंह मार्ग/Shahed Jait Singh Marg
 110 016/New Delhi-110 016

(5)	Kendriya Vidyalayas where school building is under construction	71
(6)	Kendriya Vidyalayas where school building is under planning	113
(7)	Kendriya Vidyalayas where land identified and awaiting lease / permanent grant in favour of Sangathan	53
(8)	Kendriya Vidyalayas where land yet to be identified by Sponsoring Authority	27
TOTAL		1039

At present, KVS has to construct permanent school buildings in 277 Kendriya Vidyalayas out of which in 71 Kendriya Vidyalayas, construction work is in progress and School Buildings are expected to be completed within 2-3 financial years. In 113 cases, construction of school buildings is under planning and AA&ES will be issued on receipt of plans and estimates from the construction agencies subject to availability of funds. In remaining 80 KVs, land is yet to be transferred by the sponsoring authorities (**Annexure-I**).



संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, संस्थागत क्षेत्र/18, Institutional Area
 शहीद जेठ सिंह मार्ग, Shaheed Jett Singh Marg
 नई दिल्ली-110 016/New Delhi-110 016

(c) Type of School Building

The School Building shall be categorized as under:

TYPE	CLASS UPTO	NO OF SECTIONS	STUDENTS STRENGTH
A-1	I TO XII	01	480
A	I TO XII	02	960
B	I TO XII	03	1440
C	I TO XII	04	1920

(d) Staff Quarters

Normally 17 Staff Quarters are constructed in two phases as per details given below:

TYPE	PHASE I	PHASE II
II	4	4
III	4	4
V	1	0

However, for Kendriya Vidyalayas located in hard stations / remote areas/ mock hills / disturbed areas where it is difficult to get proper accommodation up to living standards of the staff members, KVS considers



संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 13, संसद क्षेत्र/13, Institutional Area
 शहीद जैत सिंह नगर/Shahid Jai Singh Nagar
 पिन-110 016/New Delhi-110 016

construction of 100% accommodation subject to availability of adequate land and budget.

(e) **Sports Facilities**

Subject to availability of land, KVS provides following sports facilities for improvement of sports skills among the students besides teaching excellence:

- (i) PRIMARY: Play area with open spaces near primary block for play equipment like Playing Slides, Wave Slides, Swings, Sea-saw, Horizontal Ladders, Ring, Gland-slip, Climbing Apparatus, Merry-Go-Round etc.
- (ii) SENIOR SECONDARY: Hockey Field, Athletic Track, Volley ball Court, Basket Ball Court, Kho-kho Lawn, Lawn Tennis Court, Kabaddi ground, Gymnastic area etc.


(f) **Space Norms**

School Buildings of Kendriya Vidyalayas is planned on the basis approved Space Norms as given at (Annexure II).

4. SYSTEM / PROCEDURE OF EXECUTION OF WORKS

As Sangathan has no in-house agency in its own for planning, designing and execution of construction works, all the construction work of KVS are ordinarily entrusted to the following Government Agencies as Deposit Work:

- (i) CPWD
- (ii) MES
- (iii) State PWD



संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18 संस्थान क्षेत्र/18, Institutional Area
 शहीद जेठ सिंह मार्ग/Shahheed Jeet Singh Marg
 नई दिल्ली-110 016/New Delhi-110 016

However, sometime above said agencies do not undertake the construction projects. In that situation KVS does the empanelment of other agencies like Public Sector Undertakings of Central Govt. / State Govt. /Semi-Govt. by following the provisions under Rule 133(3) of GFR, 2017. After following the prescribed procedure and provisions of GFR, bids for determining lowest service charges are invited and the work is entrusted to the agencies. An agreement between KVS and the agency is also signed for designing and supervising the works.

The following stages are involved in this regard:

- (i) After transfer of land, formal request to the Chief Engineer for preparation of preliminary targets as per KVS Space Norms.
- (ii) Approval of preliminary drawings by KVS.
- (iii) Submission of preliminary estimates planned on DPAR/DSAR of CPWD and schedule of rates of MES.
- (iv) Issue of Administrative Approval and Expenditure Sanctioned (AA&ES) and release of 1st installment of funds to take up the work.
- (v) Tender action by the construction agencies
- (vi) Start of work by the contractor
- (vii) Monitoring and release of funds on monthly progress report received from the In-charge of Work duly counter signed by the Principal.
- (viii) Monitoring Committee: A Committee consisting of the following is constituted at the Vidyalaya level for regular monitoring of major / minor works sanctioned by the Kendriya Vidyalaya Sangathan:

1.	Chairman VMC or his nominee	Chairman
2.	Representatives of local unit of CPWD or MES or Railways or State PWD (one each from Civil and Electrical)	Member
3.	Representatives from nearby Civil	Member

संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin)
 केंद्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, सत्यानंद क्षेत्र/18, Institutional Area
 शहीद जीत सिंह मार्ग/Shahed Jeet Singh Marg
 Delhi-110 016


	engineering Department, Engineering College or Polytechnic	
4.	Representative of the Construction Agency	Member
5.	Teachers from the Vidyalaya (PGT-Science, SUPW Teacher, PET)	Member
6.	Principal	Member-Secretary

The meeting of the Monitoring Committee is convened once in a month to :

- Ensure timely start of work;
- Inspect quality / workmanship of construction and review progress of the work;
- Review of the schedule of the work (BAR Chart) to ensure completion of the work in time;
- Expedite handling over / taking over of completed work and rectification of defects.

(ix) Quality of construction work:

- All KVS works are entrusted to Govt. Construction Agencies viz CPWD / MES and other Central / State Public Sector Undertakings on "Deposit Work" system from concept to commissioning stage, in which construction agencies are fully responsible for planning, designing and execution with quality construction.
- Before start of work, KVS ensures that the structural drawings submitted by construction agencies (other than CPWD/MES) are vetted by IIT and Technical Sanction is accorded by their Competent Authority.
- Third Party Quality assurance by IIT/NIT/Govt. Engineering Colleges / organization is undertaken by construction agencies at various stages of construction to ascertain the quality of construction.




संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Central Board of Secondary Education
 18, संसदीय क्षेत्र/18, Institutional Area
 जय सिंह मार्ग/Shaheed Jai Singh Marg
 New Delhi-110 016

- Review of progress of work in the Works Committee Meeting: The work programme shall be approved and progress of each work is reviewed by Works Committee consisting of following members:

1.	Vice Chairperson, Kendriya Vidyalaya Sangathan	Chairperson
2.	Financial Advisor, Ministry of HRD	Member
3.	Commissioner, Kendriya Vidyalaya Sangathan	Member
4.	Director of Education (Army), Ministry of Defence	Member
5.	Director of Education (Air Force), Ministry of Defence	Member
6.	Director of Education (Navy), Ministry of Defence	Member
7.	Director, Military Land & Cantonments, Ministry of Defence	Member
8.	Engineer-in-Chief, MES, Ministry of Defence	Member
9.	Director General (works), CPWD	Member
10.	Financial Advisory, Ministry of Urban Development	Member
11.	Member (Engineering), Railway Board	Member
12.	Joint Commissioner (Finance), Kendriya Vidyalaya Sangathan	Member-Secretary

- (x) Completion of work and handing over of the project.
- (xi) Completion Report and settlement of accounts.



संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, राजमार्ग संगठन/18 Institutional Area
 शांति नगर सिटी नई दिल्ली/Peace Maid
 नई दिल्ली-110 016/New Delhi-110 016

5. ESTIMATION / PROJECT COST / FUNDING PATTERN OF THE SCHEME

In the case of CPWD, preliminary estimates are framed based on DPAR with updated cost index and in the case of MES, estimates are based on MES standard schedule of rates..

The present cost of construction of school building (2 Section each from Class I to XII) is Rs.18.23 Crore (approximately). However, this cost may vary place to place as per site conditions, availability of manpower in remote areas / North East Region and revision of cost index from time to time.

FUNDING PATTERN OF THE SCHEME:

The Govt. provides Grants for creation of Capital Assets, out of which funds are released for construction activities. AA&ES is issued along with release of 1st installment of fund to take up the work. Next installments of funds are released on submission of Physical and Financial Progress of the work in KVS format submitted by the construction agency duly counter signed by the Principal.

The tentative funding pattern of project is as under:

Financial Year	Cumulative Release of Fund
1 ST Financial year	20%
2 nd Financial year	60%
3 rd Financial year	100%

संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, संस्थागत क्षेत्र/18, Institutional Area
 शहीद जेत सिंह मार्ग/Shaheed Jeet Singh Marg
 110 016/New Delhi-110 016

PROJECTS WHICH REQUIRE FUNDING FROM HEFA.

(a) Ongoing projects :-								
S. No	STATE	NAME OF PROJECT CONSTRUCTION OF SCHOOL BUILDING AT KENDRIYA VIDYALAYA	COST OF PROJECT		TERM LOAN REQUIRED (RS. IN CRORE)	PERIOD OF EXECUTION (IN MONTHS)	REPAYMENT SOUGHT	STATUS OF THE PROJECT (ADMN/TECH APPROVALS)
			For Bldg/ Civil Structure (Rs in Crore)	For Equipment				
1	Andhra Pradesh	Tenali	16.00	...	1.81	18		AA&ES ISSUED
2	Chattisgarh	Narayanpur	16.94	...	12.74	15		AA&ES ISSUED
3	Chattisgarh	Janjgir Champa	15.97	...	3.77	12		AA&ES ISSUED
4	Himachal Pradesh	Saloh	16.21	...	16.21	18-24		AA&ES ISSUED
5	Karnataka	Chikodi	17.11	...	10.91	18		AA&ES ISSUED
6	Odisha	No.2 Sambalpur	16.46	...	14.26	16		AA&ES ISSUED
7	Rajasthan	Hanumangarh	16.05	...	7.85	18		AA&ES ISSUED
8	Telangana	Miryalaguda	15.25	...	5.05	15		AA&ES ISSUED
9	Telangana	Sirsilla	16.52	...	16.52	18-24		AA&ES ISSUED
10	Uttar Pradesh	Sharawasti	15.85	...	15.65	18-24		AA&ES ISSUED
11	Uttar Pradesh	Gangrani	16.81	...	16.6	18-24		AA&ES ISSUED
	Sub total				121.37			


संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, संस्थागत क्षेत्र/18, Institutional Area
 शहीद जीत सिंह मार्ग/Shahid Jeet Singh Marg
 नई दिल्ली-110 016/New Delhi-110 016

(b) New projects :-								
S. No	STATE	NAME OF PROJECT CONSTRUCTION OF SCHOOL BUILDING AT KENDRIYA VIDYALAYA	COST OF PROJECT		TERM LOAN REQUIRED (RS. IN CRORE)	PERIOD OF EXECUTION (IN MONTHS)	REPAYMENT SCHEDULE	STATUS OF THE PROJECT (ADMIN/TECH APPROVALS)
			For Bldg/ Civil Structure (Rs In Crore)	For Equipment				
1	Andhra Pradesh	Setenapalli	18.23	...	18.23	18-24		AA&ES Yet to be issued
2	Andhra Pradesh	Rajampalli	18.23	...	18.23	18-24		AA&ES Yet to be issued
3	Arunachal Pradesh	Longding	18.23	...	18.23	18-24		AA&ES Yet to be issued
4	Chattisgarh	Bijapur	18.23	...	18.23	18-24		AA&ES Yet to be issued
5	Chattisgarh	Kurud	18.23	...	18.23	18-24		AA&ES Yet to be issued
6	Chattisgarh	Sukma	18.23	...	18.23	18-24		AA&ES Yet to be issued
7	Chattisgarh	Naya Raipur	18.23	...	18.23	18-24		AA&ES Yet to be issued
8	Chattisgarh	Kawardha	18.23	...	18.23	18-24		AA&ES Yet to be issued
9	Chattisgarh	Saraipalli	18.23	...	18.23	18-24		AA&ES Yet to be issued
10	Gujarat	Patan	18.23	...	18.23	18-24		AA&ES Yet to be issued
11	Haryana	Samalkha	18.23	...	18.23	18-24		AA&ES Yet to be issued
12	Jharkhand	Lohardaga	18.23	...	18.23	18-24		AA&ES Yet to be issued
13	Jharkhand	Khunti	18.23	...	18.23	18-24		AA&ES Yet to be issued
14	Jharkhand	Dumka	18.23	...	18.23	18-24		AA&ES Yet to be issued
15	Jharkhand	Chatra	18.23	...	18.23	18-24		AA&ES Yet to be issued
16	Jharkhand	Giridih	18.23	...	18.23	18-24		AA&ES Yet to be issued
17	Kerala	Nileshwar	18.23	...	18.23	18-24		AA&ES Yet to be issued
18	Karnataka	Kadrimidri	18.23	...	18.23	18-24		AA&ES Yet to be issued
19	Karnataka	Chennapatna	18.23	...	18.23	18-24		AA&ES Yet to be issued


 संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन Kendriya Vidyalaya Sangathan
 12, आगत क्षेत्र, 18, 'National Area'
 सिंह मार्ग/Shaneed Jeet Singh Marg
 दिल्ली-110 016

20	Madhya Pradesh	Chanderi	18.23	...	18.23	18-24	AA&ES	Yet to be issued
21	Madhya Pradesh	Multai	18.23	...	18.23	18-24	AA&ES	Yet to be issued
22	Madhya Pradesh	Ganj Basoda	18.23	...	18.23	18-24	AA&ES	Yet to be issued
23	Madhya Pradesh	No.2 Neemuch	18.23	...	18.23	18-24	AA&ES	Yet to be issued
24	Madhya Pradesh	Dabra	18.23	...	18.23	18-24	AA&ES	Yet to be issued
25	Madhya Pradesh	Hatta Nagar	18.23	...	18.23	18-24	AA&ES	Yet to be issued
26	Orissa	Jagatsingh Pur	18.23	...	18.23	18-24	AA&ES	Yet to be issued
27	Rajasthan	Nagaur	18.23	...	18.23	18-24	AA&ES	Yet to be issued
28	Rajasthan	CISF Jaipur	18.23	...	18.23	18-24	AA&ES	Yet to be issued
29	Rajasthan	Dhaulpur	18.23	...	18.23	18-24	AA&ES	Yet to be issued
30	Telangana	Bhongir	18.23	...	18.23	18-24	AA&ES	Yet to be issued
31	West Bengal	Rly Kharagpur	18.23	...	18.23	18-24	AA&ES	Yet to be issued


(c) Details of KVs approved by CCEA, GoI for opening ; but could not be opened for want of funds

32	Karnataka	Virupapura Village, Gangavathi Taluk, distt Koppal	18.23	...	18.23	18-24	AA&ES	Yet to be issued
33	Kerela	Konni, Distt Pathanamthitta	18.23	...	18.23	18-24	AA&ES	Yet to be issued
34	Madhya Pradesh	Lakhnadon Distt Seoni	18.23	...	18.23	18-24	AA&ES	Yet to be issued
35	Rajasthan	Tivri, Distt Jodhpur	18.23	...	18.23	18-24	AA&ES	Yet to be issued
36	Rajasthan	Pali, Distt Pali	18.23	...	18.23	18-24	AA&ES	Yet to be issued
37	Telangana	Nizamabad, Distt Nizamabad	18.23	...	18.23	18-24	AA&ES	Yet to be issued

संजय कुमार / SANJAY KUMAR
 सहायक कमिश्नर (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, संख्या 18, Institutional Area
 शहीद जीत सिंह मार्ग/Shaneed Jeet Singh Marg
 नई दिल्ली-110 016/New Delhi-110 016

(d) Proposal submitted by MHRD to CCEA for opening of 13 KV's during the year 2018-19.

38	Bihar	Devkund, Distt Aurangabad	18.23	...	18.23	18-24	AA&ES Yet to be issued
39	Bihar	Nawada, Distt Nawada LWE	18.23	...	18.23	18-24	AA&ES Yet to be issued
40	Jharkhand	Palamau, Distt Palamau LWE	18.23	...	18.23	18-24	AA&ES Yet to be issued
41	Karnataka	Kudamalaku nte, Gauribidanu r, Distt Chikkaballa pur	18.23	...	18.23	18-24	AA&ES Yet to be issued
42	Maharashtra	Parbhani, Distt Parbhani	18.23	...	18.23	18-24	AA&ES Yet to be issued
43	Maharashtra	Washim, Distt Washim	18.23	...	18.23	18-24	AA&ES Yet to be issued
44	Manipur	Chakpikaron g, Chandel Distt	18.23	...	18.23	18-24	AA&ES Yet to be issued
45	Telangana	Siddipet, distt Siddipet	18.23	...	18.23	18-24	AA&ES Yet to be issued
46	Uttar Pradesh	Banda, Distt Banda	18.23	...	18.23	18-24	AA&ES Yet to be issued
47	Uttar Pradesh	Baoli, Bagpat, Distt Bagpat	18.23	...	18.23	18-24	AA&ES Yet to be issued
48	Uttar Pradesh	Bhadohi	18.23	...	18.23	18-24	AA&ES Yet to be issued
49	Uttar Pradesh	Distt Mirzapur	18.23	...	18.23	18-24	AA&ES Yet to be issued
50	Uttar Pradesh	SSG, CISF Surajpur, Greater Noida	18.23	...	18.23	18-24	AA&ES Yet to be issued
Total					911.5		


 संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय वित्त मंत्रालय/Ministry of Finance, Government of India
 18, संजयपुर रोड/18, Sanjaypur Road
 नई दिल्ली-110 016/New Delhi-110 016


6. COMPONENTS OF THE SCHEME

A comprehensive infrastructure involves the following facilities:

- (a) Construction of school building
- (b) Sports facilities
- (c) Staff Quarters
- (d) Campus Development
- (e) Compound wall with sentry post
- (f) External water supply & Electric connection
- (g) Canteen, cycle stand
- (h) Fire fighting as per NBC Guidelines
- (i) Water Harvesting
- (j) Adopting NDMA Guidelines
- (k) Ramp & Special toilets for persons with disabilities (Divyaang children)
- (l) Follow Accessible India Campaign (सुगम्य भारत अभियान)
- (m) Green Building Norms proper architectural planning and provisions of LED/BEE 5 star rating appliances.

7. SCHEDULE OF IMPLEMENTATION

ACTIVITY	TENTATIVE TIME REQUIRED
Submission of preliminary drawings	3 Months
Submission of Preliminary Estimates after approval of Preliminary Drawings and issue of AA&ES with release of 1 st installment of funds	3 Months


 संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin)
 केन्द्रीय अर्थसूचना/केंद्रीय विद्यालय संगठन
 18, सरकारी क्षेत्र, 18, Institutional Area
 शहीद जय प्रकाश मार्ग, शहीद जय प्रकाश मार्ग
 नई दिल्ली-110 015 / New Delhi-110 015

Preparation of Detailed estimates, finalization of tenders	6-9 Months*	
Execution Period	18-24 Months**	

*Depends upon location of work and response to tenders and availability of funds.

** Depends upon the location.

8. BUDGET REQUIREMENT / ALLOCATION OF BUDGET FOR THE SCHEME FINANCIAL ASSISTANCE

For establishment and running of the Kendriya Vidyalayas across the country, Government of India provides financial support to the KVS in the form of Grants in Aid under three distinct heads – ‘Salary’, ‘General’ and ‘Creation Capital Assets’. In addition, KVS generates funds by collecting user charges from students.


Major components under ‘Salary’, ‘General’ and ‘Creation of Capital Assets’

Salary

Besides salary of teaching and non-teaching staff, the expenditure on leave encashment, TA, LTC, Medical reimbursement and CEA are met from the GIA (Salaries).

General

Besides payment of pension, retirement benefits (gratuity, commutation of pension, leave encashment etc.) the management contribution to CPF, contribution to the New Pension System as well as expenditure on repairs and maintenance is met out from GIA ‘General’.



संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, संयोग नगर/18, Institutional Area
 शहीद जीत सिंह मार्ग/Shaheed Jeet Singh Marg
 → दिल्ली-110 016/New Delhi-110 016

Creation of Capital Assets

Expenditure relating to civil works and computerization is booked to the budget allocation under GIA 'Creation of Capital Assets'.

(a) Details of Plan and Non- Plan expenditure.

(Rs. in Crore)

Year	Plan		Non plan	
	Grant Received	Expenditure	Grant Received	Expenditure
2012-13	350.00	320.23	2104.34	2341.66
2013-14	350.00	351.00	2424.97	2627.33
2014-15	742.00	734.72	2501.15	2617.40
2015-16	875.00	896.37	2403.47	2796.76
2016-17	1102.71	1085.28	2884.54	2896.60

(b) Annual Plan Allocation for the year 2017-18,2018-19

(Rs. in crore)

YEAR	Revenue	Creation of Capital Assets	Total
RE 2017-18	4323.01	674.24	4997.25
BE 2018-19	4193.35	231.35	4425.00




संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18 संस्थान क्षेत्र/18. Institutional Area
 शाहूजी विहार मजरा/Shaheed Jai Singh Vihar
 नई दिल्ली-110 016/New Delhi-110 016

(c) Fee Structure (per Month) w.e.f. 01.04.2013

1.	Admission Fee	Rs. 25.00
2.	Re Admission Fee	Rs 100.00
3.	Tuition Fee	
3(a)	Class IX & X (Boys)	Rs 200.00
3(b)	Class XI & XII Commerce & Humanities (Boys)	Rs 300.00
3(c)	Class XI & XII Science (Boys)	Rs.400.00
4.	Computer Fund	
4(a)	Class III onwards wherever Computer Education is being imparted	Rs 100.00
4(b)	Computer Science Fee. (for elective subjects) + 2 stage	Rs 150.00
5.	Vidyalaya Vikas Nidhi	
5(a)	Class I – XII	Rs 500.00

Category wise exemption of payment of Tuition fee, VVN and Computer Fund

Category	Tuition fees	Computer Fund	VVN Contribution
Girls students from class I-XII	Exempted	Not Exempted	Not Exempted
SC/ST students	Exempted	Not Exempted	Not Exempted
Children of KVS employees	Exempted	Not Exempted	Not Exempted
Children of officers and men of armed forces and Paramilitary personnel killed or disabled during the hostilities 1962;1965;1971 and 1999 and as well as to the children of Defence Personnel of Indian Peace Keeping Force(IPKF) in Srilanka and personnel of armed forces killed or disabled in "Operation Meghdoot" in Seachen area and "Operation Vijay" in Kargil. In addition, the concession of exemption from payment of tuition fee, VVN and Computer fund to the children of Armed Forces and Para Military Forces	Exempted	Not Exempted	Exempted



संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 15, नन्दलोक क्षेत्र/15, Institutional Area
 शा. म. म. शहीद जे. ए. आर. आर. 110 016
 110 016/New Delhi-110 016

personnel whose parents were killed/declared missing or permanently disabled during any counter insurgency operation in India or abroad has also been extended. This exemption may be granted after certification by the concerned Ministry.			
Children of the parents, who are living below poverty line, up to two children and having BPL card	Exempted		
Disabled students. (Subject to the condition laid down in KVS Letter No.F125-19/2007-08/KVS (Budget) dt.15.10.2009).	Exempted	Not Exempted	Exempted
All girl students from classes VI to XII who happen to be the only child of their parents (w.e.f. 01.01.2006 from VVN & Computer Fund.)	Exempted	Exempted	Exempted
Emergency Assistance to the students	Exemption of VVN for one academic session is allowed		

Note:

- Exemption of various types of fees mentioned above will not be allowed henceforth to the children of Government employeess as they are getting reimbursement from their departments.
- KVs under project Sector, are authorized to implement their own differential fee structure vide KVS Letter No. 6-1/91-KVS(Budget) dt.11.11.1999


As regard to KVs under project Sector, they are authorized to implement their own differential fee structure vide KVS Letter No. 6-1/91-KVS (Budget) dt.11.11.1999.

JK

संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, संस्थागत क्षेत्र/18, Institutional Area
 शहीद जीत सिंह मार्ग/Shahheed Jeet Singh Marg
 नई दिल्ली-110 016/New Delhi-110 016

9. CONCLUSION

At the beginning when KVS came into existence, the motive of this organization was to provide uninterrupted education to the wards of transferable Central Government employees. But in today's scenario Kendriya Vidyalaya Sangathan has proven itself as a pace setting organization in the field of School education as well as sports and extra curriculum activities. Apart from Central Government employees, parents from all sections of the society prefer their wards to study in the Kendriya Vidyalayas. Considering all these factors, there is a requirement to provide safe buildings containing all the infrastructural facilities for all the functional Kendriya Vidyalayas running all over the country and to undertake maintenance / expansion of the existing buildings as per day to day requirements as elaborated in this report in pursuit of excellence in education.


 संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त) / Assistant Commissioner (Fin)
 केन्द्रीय विद्यालय संगठन / Kendriya Vidyalaya Sangathan
 18, संस्थागत क्षेत्र / 1E, Institutional Area
 शहीद जीत सिंह मार्ग / Shaned Jeet Singh Marg
 नई दिल्ली-110 016 / New Delhi-110 016

01.05.2018 को चल रहे विद्यालय भवनों के निर्माण कार्य की स्थिति / Status of on going Construction Work of School Building Projects as on राज्य वार / State-Wise

क्र० संख्या / Sl. No	के० वि० का नाम / Name of Kendriya Vidyalaya	AA&ES की राशि / (₹ लाख में) / AA&ES (Rs. in lakh)	संस्वीकृति की तारीख / Date of sanction	निर्माण एजेंसी / Constrction Agency	कार्य प्रारम्भ करने की तारीख / Date of start	कार्य की प्रगति का प्रतिशत / Physical Progress upto date	कार्य पूर्ण होने की अनुबंधित तारीख / Stipulated Date of Completion	30.04.2018 तक निर्मुक्त राशि (₹ लाख में) / Amount released till 30.04..2018 (Rs. in lakh)	शेष देयता (₹ लाख में) / Balance Liablity (Rs. in lakh)	BE 2018-19 (In Lakh)	BE 2019-20 (In Lakh)	टिप्पणी/ Remarks
13												
आन्ध्र प्रदेश / Andhra Pradesh												
1	Tenali ('A' Type + 09 SQ + BW)	1600.94	05.10.2015	HSCL	17.02.16	70%	16.08.17	1420.00	180.94	180.00	0.94	work in progress. TDC-30.06.18.
अरुणाचल प्रदेश / Arunachal Pradesh												
2	Miao (A-I+09 SQ+BW)	2383.70	13.01.2015	AP PWD	01.08.15	40%	28.02.18	1700.00	683.70	600.00	83.70	Slow Progress due to N.E. Region problem
3	Tuting (A-I+09 SQ+BW)	2431.81	12.10.2015	AP PWD	10.01.16	45%	March, 2018	1320.00	1111.81	1000.00	111.81	Slow Progress due to N.E. Region problem
असम / Assam												
4	Rangiya (B- Type+SB + B/w)	2264.95	01.09.2016 03.05.2017	AP PWD	16.01.17	50%	31.08.18	2020.00	244.95	240.00	4.95	Work in progress.
बिहार / Bihar												
5	Aniwan, Jehanabad ('B'-Type+09 SQ)	2679.99	04.12.2014	CPWD	19.08.15	76%	18.02.17	1920.00	759.99	750.00	9.99	Initial delay due to land dispute. TDC-30.06.2018
6	Araria ('A'-Type+09 SQ + BW)	1535.45	25.03.2015	CPWD	02.04.16	80%	01.04.17	1420.00	115.45	110.00	5.45	Slow progress by CPWD. TDC- 30.06.18.
7	Betia ('A'- Type+BW)	1301.66	24.06.2014	HSCL	25.07.14	88%	31.01.16	1120.00	181.66	180.00	1.66	Due to Bandh & Ban on sand. TDC-30.09.2018
8	Bela ('A'- SB+09SQ+BW+Cov. CC)	2001.95	22.11.2016	CPWD	220.00	1781.95	1000.00	781.95	Work recently sanctioned and at tender stage
9	Harnaut ('A' Type+09SQ+BW)	2015.01	16.05.2017	CPWD	20.00	1995.01	1000.00	995.01	Stop Order issued
छत्तीसगढ़ / Chhatisgarh												
10	Narayanpur ('A'-Type+09 SQ + BW)	1694.01	20.06.2016 01.03.2017	BBJ&JCC	30.05.17	21%	Aug, 2018	420.00	1274.01	1000.00	274.01	Delay on the part of Construction Agency in completing the formalities. Go ahead approval given on 01.03.17
11	Rajnandgaon ('A'-Type+SB+09 SQ + BW)	1625.93	24.08.2016	CPWD	17.12.16	85%	16.12.17	1320.00	305.93	300.00	5.93	work in progress. Shortage of funds.

**01.05.2018 को चल रहे विद्यालय भवनों के निर्माण कार्य की स्थिति / Status of on going Construction Work of School Building Projects as on
राज्य वार / State-Wise**

क्र० संख्या / Sl. No	के० वि० का नाम / Name of Kendriya Vidyalaya	AA&ES की राशि / (₹ लाख में) / AA&ES (Rs. in lakh)	संस्वीकृति की तारीख / Date of sanction	निर्माण एजेंसी / Constrction Agency	कार्य प्रारम्भ करने की तारीख / Date of start	कार्य की प्रगति का प्रतिशत / Physical Progress upto date	कार्य पूर्ण होने की अनुबंधित तारीख / Stipulated Date of Completion	30.04.2018 तक निर्मुक्त राशि (₹ लाख में) / Amount released till 30.04.2018 (Rs. in lakh)	शेष देयता (₹ लाख में) / Balance Liability (Rs. in lakh)	BE 2018-19 (In Lakh)	BE 2019-20 (In Lakh)	टिप्पणी / Remarks
1	2	3	4	5	6	7	8	9	10			13
12	Hasaud (Janjgir) ('A'-Type+SB+09 SQ + BW)	1597.03	01.09.2016	CPWD	24.11.16	75%	23.11.17	1220.00	377.03	370.00	7.03	work in progress. TDC-30.06.18
13	No. 4 BCPP Korba ('A'-Type+SB+09 SQ + BW)	1586.32	01.09.2016	CPWD	24.11.16	75%	23.11.17	1220.00	366.32	360	6.32	work in progress
दिल्ली / Delhi												
14	Sec.-22, Rohini ('B' Type)	746.11	03.10.2007	CPWD	Work yet to start	25.00	721.11	500.00	221.11	Drawing yet to be approved by local bodies. Permission for demolition of temporary structure awaited
15	Sec.-28, Rohini ('B' Type S/B)	1800.62	12.08.2014	AP PWD	08.12.17	18%	07.12.19	620.00	1180.62	800.00	380.62	Delay in approval of Drawings by MCD
16	Shahdara ('A' Type S/B)	1460.12	13.04.2018	CPWD				500.00	960.12	500.00	460.12	Work recently sanctioned.
गुजरात / Gujarat												
17	Dahod ('A' Type + 09 SQ + BW)	1589.37	09.06.2015	CPWD	26.07.16	75%	25.10.17	820.00	769.37	760.00	9.37	Initial delay on the part of CPWD.
18	Jetpur ('A-1' Type + 09 SQ + BW)	1252.79	27.05.2015	CPWD	22.07.16	75%	21.10.17	820.00	432.79	430.00	2.79	Initial delay on the part of CPWD. TDC-30.06.18.
19	Viramgaon ('A-1' Type + BW)	1225.36	08.10.2014	CPWD	21.09.15	80%	20.09.16	1020.00	205.36	200.00	5.36	Initial delay due to land problem.
हरियाणा / Haryana												
20	No.3 Faridabad ('B' Type SB+ 9SQ+BW)	2018.22	01.03.2017	DHPD	11.10.17	29%	10.10.19	820.00	1198.22	800.00	398.22	Work in progress
21	Budayan (Jind) ('B' Type SB+ 9SQ)	1943.68	26.04.17	CPWD	06.03.18	Started	29.05.19	720.00	1223.68	800.00	423.68	Recently started
हिमाचल प्रदेश / Himanchal Pradesh												
22	Saloh ('A' Type + 09 SQ)	1620.95	21.06.2017	BSNL		1620.95	800.00	820.95	IT vetting is awaited from BSNL to issue goahead.
जम्मू एवं कश्मीर / Jammu & Kashmir												
23	B.S.F Bandipur ('A-1' SB+ 09SQ + BW)	1606.94	27.07.16	CPWD	30.05.17	5%	29.05.19	420.00	1186.94	1000.00	186.94	Work in progress

-27-

संयम कुमारी (वि०) Assistant Secretary to Government of India
Kendriya Vidyalaya, New Delhi

01.05.2018 को चल रहे विद्यालय भवनों के निर्माण कार्य की स्थिति / Status of on going Construction Work of School Building Projects as on राज्य वार / State-Wise

क्र० संख्या / Sl. No	के० वि० का नाम / Name of Kendriya Vidyalaya	AA&ES की राशि / (₹ लाख में) / AA&ES (Rs. in lakh)	संस्वीकृति की तारीख / Date of sanction	निर्माण एजेंसी / Constrcti on Agency	कार्य प्रारम्भ करने की तारीख / Date of start	कार्य की प्रगति का प्रतिशत / Physical Progress upto date	कार्य पूर्ण होने की अनुबंधित तारीख / Stipulated Date of Completion	30.04.2018 तक निर्मुक्त राशि (₹ लाख में) / Amount released till 30.04..2018 (Rs. in lakh)	शेष देयता (₹ लाख में) / Balance Liablity (Rs. in lakh)	BE 2018-19 (In Lakh)	BE 2019-20 (In Lakh)	टिप्पणी/ Remarks
1	2	3	4	5	6	7	8	9	10			13
24	Kargil (A - Type BW)	1372.63	01.03.2013	CPWD	15.08.14	80%	14.08.17	920.00	452.63	450.00	2.63	Delay due to J&K Problem.
25	Miran Sahib ('A' Type+09 SQ+BW)	2017.63	09.01.2017	CPWD	17.07.17	5%	16.01.19	620.00	1397.63	800.00	597.63	Work in progress
झारखण्ड / Jharkhand												
26	Godda ('A' Type + 09 SQ + BW)	1773.64	15.07.2015	CPWD	24.11.15	88%	23.11.16	1620.00	153.64	150.00	3.64	TDC- 30.06.18
कर्नाटक / Karnataka												
27	Kodagu ('A'- Type+09 SQ+ BW)	1267.79	20.10.2015	CPWD	01.10.16	68%	17.04.18	1220.00	47.79	40.00	7.79	Work in progress. TDC-30.09.18
28	Koppal ('A' - Type+09 SQ+ BW)	1713.94	12.09.2014	HSCL	10.12.15	55%	12.06.17 TDC-30.09.18	1020.00	693.94	690.00	3.94	Initial delay on account of dispute on land boundaries.
29	Haveri ('A'- Type+09 SQ+ BW)	2061.80	01.09.2016	FEDO	0.00	2061.80	1200.00	861.80	Stop Order issued
30	Chikodi ('A'- Type+09 SQ+ BW)	1710.97	29.03.2017	CPWD	08.08.17	18%	10.02.19	620.00	1090.97	1000.00	90.97	Work recently sanctioned
केरल/Kerala												
31	Ezhimala ('A' Type + BW)	1991.24	24.04.2015	MES	17.08.17	7%	17.07.19	220.00	1771.24	1000.00	771.24	Delayed on the part of MES.
32	Kanhagad ('A' Type+ 09 SQ+BW + covering)	2235.49	02.11.2015	CPWD	01.10.16	50%	28.12.17	1020.00	1215.49	1200.00	15.49	Delay due to dispute. TDC-30.09.18
33	KPA, Ramavarmapuram ('B' Type SB+ 09 SQ+BW + covering of cent. courtyard)	2664.40	20.07.2016	CPWD	320.00	2344.40	1300.00	1044.40	Work at tender stage.
34	SAP, Trivandrum ('B' Type + BW)	2170.18	22.05.2014	CPWD	23.03.16	73%	15.06.17	1820.00	350.18	350.18	0.00	Slow progress due to shortage of funds TDC- 30.06.2018.

28

संजय कुमार / SANJAY KUMAR
 सहायक निदेशक (निर्माण)/Assistant C
 केन्द्रीय विद्यालय संगठन/Ke
 18, संस्थान भवन
 शरीर

01.05.2018 को चल रहे विद्यालय भवनों के निर्माण कार्य की स्थिति / Status of on going Construction Work of School Building Projects as on राज्य वार / State-Wise

क्र० संख्या / Sl. No	के० वि० का नाम / Name of Kendriya Vidyalaya	AA&ES की राशि / (₹ लाख में) / AA&ES (Rs. in lakh)	संस्वीकृति की तारीख / Date of sanction	निर्माण एजेंसी / Constrcti on Agency	कार्य प्रारम्भ करने की तारीख / Date of start	कार्य की प्रगति का प्रतिशत / Physical Progress upto date	कार्य पूर्ण होने की अनुबंधित तारीख / Stipulated Date of Completion	30.042018 तक निर्मुक्त राशि (₹ लाख में) / Amount released till 30.04.2018 (Rs. in lakh)	शेष देयता (₹ लाख में) / Balance Liabltiy (Rs. in lakh)	BE 2018-19 (In Lakh)	BE 2019-20 (In Lakh)	टिप्पणी/ Remarks
1	2	3	4	5	6	7	8	9	10			13
35	Kaduruthy ('A' Type SB+ 09 SQ+BW + covering of central	3020.62	27.12.2016	FEDO	...	0%	...	0.00	3020.62	1200.00	1820.62	Stop Order issued
लक्षद्वीप / Lakshdeep												
36	Kavarati ('A+' Type + 11 SQ + BW)	2325.64	02.02.2015	CPWD	12.02.16	65%	04.08.17	1620.00	705.64	700.00	5.64	Initial slow progress. Now progressing well. TDC- 30.06.18
मध्य प्रदेश / Madhya Pradesh												
37	Betul ('A'- Type SB +09 sq +BW +Covering of courtyard)	1647.29	20.07.16	CPWD	02.12.16	65%	01.02.18	1020.00	627.29	600.00	27.29	Slow progress /Shortage of funds
38	Chaurai ('A'-Type + 9 SQ + BW)	1284.56	17.06.15	CPWD	25.03.16	36%	24.03.17	620.00	664.56	650.00	14.56	Slow progress /Shortage of funds. TDC- 30.09.2018
39	No.2 Chhindwada ('A' type SB+ 09SQ + BW+ Cov.of Court Yard)	1462.89	21.07.16	CPWD	01.01.17	19%	31.12.17	620.00	842.89	800.00	42.89	Work is being started shortly.TDC- 31.12.2018.
40	Datia ('B'- Type SB +09 SQ +BW Covering of central courtyard)	1934.54	21.7.16	CPWD	27.12.16	83%	26.03.18	1420.00	514.54	500.00	14.54	Work in progress
41	Dindori ('A'- Type SB +09 SQ +BW Covering of courtyard)	1604.72	21.7.16	CPWD	01.01.2017	65%	31.12.17	1020.00	584.72	550.00	34.72	Workin progress. TDC-30.06.18.
42	No.-2, Satna ('A'- Type+SQ+BW)	1926.35	07.12.2015 20.12.2016	UPJN	03.01.17	50%	02.01.19	1020.00	906.35	900.00	6.35	work in progress
43	Tikamgarh ('A'- Type SB+09SQ+ BW+ Covering of Courtyard)	1390.21	20.07.16	CPWD	27.12.16	85%	26.12.2017	1020.00	370.21	350.00	20.21	Work in progress
44	Harda ('A'- Type+9SQ+BW)	1651.25	19.09.2016	FEDO	...	0%	...	0.00	1651.25	1000.00	651.25	Stop Order issued

-5-

30.04.2018
के० वि० के निर्माण कार्य की स्थिति / Status of on going Construction Work of School Building Projects as on राज्य वार / State-Wise

01.05.2018 को चल रहे विद्यालय भवनों के निर्माण कार्य की स्थिति / Status of on going Construction Work of School Building Projects as on राज्य वार / State-Wise

क्र० संख्या / Sl. No	के० वि० का नाम / Name of Kendriya Vidyalaya	AA&ES की राशि / (₹ लाख में) / AA&ES (Rs. in lakh)	संस्वीकृति की तारीख / Date of sanction	निर्माण एजेंसी / Constrcti on Agency	कार्य प्रारम्भ करने की तारीख / Date of start	कार्य की प्रगति का प्रतिशत / Physical Progress upto date	कार्य पूर्ण होने की अनुबंधित तारीख / Stipulated Date of Completion	30.04.2018 तक निर्मुक्त राशि (₹ लाख में) / Amount released till 30.04..2018 (Rs. in lakh)	शेष देयता (₹ लाख में) / Balance Liability (Rs. in lakh)	BE 2018-19 (In Lakh)	BE 2019-20 (In Lakh)	टिप्पणी/ Remarks
1	2	3	4	5	6	7	8	9	10			13
45	MalanjKhand Type SB +9 SQ+BW) ('A-	1831.62	28.06.2017	UPJN	...	0%	...	0.00	1831.62	1100.00	731.62	Stop Order issued
महाराष्ट्र / Maharashtra												
46	Nanded ('A' Type+ 09 SQ + BW)	2276.52	08.09.2016	UPJN	15.09.16	70%	14.09.18	1820.00	456.52	450.00	6.52	work in progress.
47	BSF, Chakur ('A' Type+ 09 SQ + BW)	1794.90	01.03.2017	UPJN	21.03.17	35%	20.03.2019	1220.00	574.90	570.00	4.90	work in progress.
मिजोरम / Mizoram												
48	Champai ('A' Type+ 09 SQ + BW)	2723.98	18.02.2015	CPWD	10.07.16	48%	01.03.18	2420.00	303.98	300.00	3.98	N.E. Region problem
49	Lunglai ('A' Type+ 09 SQ + BW)	2385.37	24.11.2014 02.05.2017	MAMCO	20.00	2365.37	1500.00	865.37	Stop Order issued
ओडिशा / Odisha												
50	Nayagarh ('A'- Type, SB +09 SQ+ BW + Covering of Courtyard)	1639.01	28.07.16	CPWD	13.12.16	65%	12.12.17	1020.00	619.01	600.00	19.01	Work in progress
51	No. 2 Sambalpur ('A' Type + 09 SQ + BW)	1646.17	01.03.17	BBJ&JCC	14.04.17	35%	Aug, 2018	420.00	1226.17	1000.00	226.17	Work in progress
52	Mahuldihha ('A' Type + 09 SQ)	1605.28	07.04.17	CPWD	25.08.17	30%	24.08.18	820.00	785.28	750.00	35.28	Work in progress
53	Aska ('A' Type SB+ 09 SQ+BW)	1701.86	16.05.17	CPWD	21.08.17	10%	20.01.19	620.00	1081.86	800.00	281.86	Work in progress

संजय कुमार / SANJAY KUMAR
 सहायक निदेशक / Assistant Director
 केंद्रीय विद्यालयों के निर्माण कार्य / Construction of Kendriya Vidyalaya
 नई दिल्ली / New Delhi

**01.05.2018 को चला रहे विद्यालय भवनों के निर्माण कार्य की स्थिति / Status of on going Construction Work of School Building Projects as on
राज्य वार / State-Wise**

क्र० संख्या / Sl. No	के० वि० का नाम / Name of Kendriya Vidyalaya	AA&ES की राशि / (₹ लाख में) / AA&ES (Rs. in lakh)	संस्वीकृति की तारीख / Date of sanction	निर्माण एजेंसी / Construct on Agency	कार्य प्रारम्भ करने की तारीख / Date of start	कार्य की प्रगति का प्रतिशत / Physical Progress upto date	कार्य पूर्ण होने की अनुबंधित तारीख / Stipulated Date of Completion	30.04.2018 तक निर्मुक्त राशि (₹ लाख में) / Amount released till 30.04.2018 (Rs. in lakh)	शेष देयता (₹ लाख में) / Balance Liability (Rs. in lakh)	BE 2018-19 (In Lakh)	BE 2019-20 (In Lakh)	टिप्पणी / Remarks
1	2	3	4	5	6	7	8	9	10			13
पुडुचेरी / Puducherry												
54	Mahe ('A-1' Type + BW)	1837.52	02.11.2015	CPWD	27.07.17	25%	21.07.2018	820.00	1017.52	1000.00	17.52	Matter is being resolved by Principal. Work suspended due to intervention of local public. TDC-26.09.18.
राजस्थान / Rajasthan												
55	Hanumangarh ('A' Type + 09 SQ + BW)	1605.31	06.10.2015 28.06.2016 (E.)	HSCL	23.11.16	55%	23.05.18	820.00	785.31	750.00	35.31	work in progress
56	Jalore ('B' Type + 09 SQ + BW)	2028.68	19.07.2016	UPSCIDCO	27.09.16	40%	31.03.18	1020.00	1008.68	1000.00	8.68	work in progress. TDC-31.07.18
57	Devgarh ('A' Type SB + 09 SQ)	1436.72	16.05.2017	CPWD	20.00	1416.72	1000.00	416.72	Stop Order issued
58	Tonk ('A-1' Type SB + 09 SQ)	1011.80	21.06.2017	CPWD	20.00	991.80	700.00	291.80	Stop Order issued
तमिलनाडु / Tamilnadu												
59	AFS, Tanjavur ('A' Type + 09 SQ + BW)	1835.53	02.11.2015	MES	20.00	1815.59	1000.00	815.59	Delay on the part of MES
60	Perambalur ('A' Type + 09 SQ + BW + Courtyard covering)	1874.02	20.07.16	CPWD	03.01.17	55%	23.04.18	920.00	954.02	900.00	54.02	work in progress
तेलंगाना / Telangana												
61	Miryalguda ('A' Type + 09 SQ + BW)	1525.03	23.02.2016	HSCL	10.12.15	55%	09.03.17	1020.00	505.03	500.00	5.03	work in progress. initial delay due to land problem. TDC-30.09.18

01.05.2018 को चल रहे विद्यालय भवनों के निर्माण कार्य की स्थिति / Status of on going Construction Work of School Building Projects as on राज्य वार / State-Wise

क्र० संख्या / SI No	के० वि० का नाम / Name of Kendriya Vidyalaya	AA&ES की राशि / (₹ लाख में) / AA&ES (Rs. in lakh)	संस्वीकृति की तारीख / Date of sanction	निर्माण एजेंसी / Constructi on Agency	कार्य प्रारम्भ करने की तारीख / Date of start	कार्य की प्रगति का प्रतिशत / Physical Progress upto date	कार्य पूर्ण होने की अनुबंधित तारीख / Stipulated Date of Completion	30.04.2018 तक निर्मुक्त राशि (₹ लाख में) / Amount released till 30.04..2018 (Rs. in lakh)	शेष देयता (₹ लाख में) / Balance Liablity (Rs. in lakh)	BE 2018-19 (In Lakh)	BE 2019-20 (In Lakh)	टिप्पणी / Remarks
1	2	3	4	5	6	7	8	9	10			13
62	Sirsilla ('A' Type SB+ 09 SQ + BW)	1651.61	16.03.2017	HSCL		1651.61	1000.00	651.61	Stop Order issued
उत्तर प्रदेश / Uttar Pradesh												
63	Deoria ('A' Type + 09 SQ + BW)	1415.74	25.06.2013	CPWD	...	Work yet to start	...	70.00	1345.74	500.00	845.74	Encroachment on land.
64	No.-4, Varanasi ('A' Type + 09 SQ + BW)	1369.52	24.11.2014	HSCL	25.05.15	B/W work done	10.11.16	220.00	1149.52	800.00	349.52	Go-ahead issued to restart the work
65	Sharawasti ('A' Type + 09 SQ + BW)	1585.12	07.04.2017	BBJ&JCC	220.00	1365.12	800.00	565.12	Go-ahead issued to restart the work on 26.03.18
66	Gangarani, Kushinagar (B Type SB + 09 SQ+BW)	1680.66	26.04.17	CPWD	20.00	1660.66	1000.00	660.66	Stop Order issued
67	Siddarthnagar (B Type SB + 09 SQ+BW)	1820.28	16.05.17	CFWD	220.00	1600.28	1000.00	600.28	Works recently sanctioned. Work held up due to HT line in LOP
उत्तराखण्ड / Uttarakhand												
68	Bhimtal (A Type SB + BW+ Covering)	1792.79	21.03.2017	CPWD	20.00	1772.79	1000.00	772.79	Stop Order issued
69	Gopeshwar ('A-1' Type SB+ 09 SQ+B/W)	2185.97	26.06.2017	JPJN		2185.97	1000.00	1185.97	Stop Order issued
पश्चिम बंगाल / West Bengal												
70	Balurghat ('A' Type+ 11 SQ + BW)	1978.34	26.06.2014	CPWD	23.01.16	80%	22.05.17	1520.00	458.34	450.00	8.34	Delay in handing over of land TDC. 30.06.18
71	Kalimpong ('A-1' Type+ BW)	1430.74	10.12.14	MES	...	9%	...	420.00	1010.74	800.00	210.74	Slow Progress
	TOTAL	126880.84						54595.00	72285.84	51380.18	20905.66	

--32--

संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (आ) / Assistant Commissioner
 राज्य विद्यालय निर्माण विभाग / Institutional
 विभाग, के० वि० सं० 13, शांति नगर, दिल्ली-110016/New

के० वि० जिनके भवन योजनाधीन / LIST OF KENDRIYA VIDYALAYAS WHERE SCHOOL BUILDING IS UNDER PLANNING as on 01-05-2018

Sr. No.	Name of KV/State	Year of opening	Type of School Building	Construction Agency	Request made on
आन्ध्र प्रदेश / Andhra Pradesh					
1	Rajampet*	2016-17	'A'
2	Kakinada*	2016-17	'A'
3	Satenapalli#	2017-18	'A'
4	Rajampalli#	2017-18
अरुणाचल प्रदेश / Arunachal Pradesh					
5	Ziro (Hapoll)*	2015-16	'A'	CE(CZ-A), APPWD, Itanagar	August, 2016
6	Longling#	2017-18	'A'
7	Roing	2003-04
असम / Assam					
8	Udalguri	2010-11	'A'	CE(NEZ), CPWD, Shillong	August, 2016
9	Barpeta	2003-04	'A'	CE(NEZ), CPWD, Shillong	April, 2015
10	Dibrugarh	2003-04	'A'	CF(NF7), CPWD, Shillong	June, 2016
बिहार / Bihar					
11	Jhajha*	2015-16	C'	CE(EZ-II), CPWD, Patna	August, 2015
छत्तीसगढ़ / Chhatisgarh					
12	Bijapur#	2017-18	A-I'
13	Kurud#	2017-18
14	Sukma#	2017-18
15	Naya Raipur#	2017-18
16	Kawardha#	2017-18
17	Saraipalli#	2017-18
दादर एवं नगर हवेली / Dadar and Nagar Haveli					
18	Silvasa	2000-01	'A'	CE(WZ-IV), CPWD, Gandhinagar	April, 2015
दमन एवं दियू / Daman & Diu					
19	Diu	2003-04	'A'	CE(WZ-IV), CPWD, Gandhinagar	August, 2016
गुजरात / Gujarat					
20	Godhra	2006-07	'A'	CE(WZ-IV), CPWD, Gandhinagar	Sep. 2008
21	Patan#	2017-18
हरियाणा / Haryana					
22	Mathana*	2016-17	'A'	CE(NZ-I), CPWD, Chandigarh	August, 2016 (BW sanctioned)
23	Fatehabad*	2017-18	B'
24	Matanhail*	2017-18	B'
25	No. IV, Ambala	2017-18	B'	CE, MES, Chandigarh	September, 2017
26	Samalkhal	2017-18

सजय कुमार / SANJAY KUMAR
 सहायक संचालक (विन)/Assistant Commissioner
 केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
 18, संजयपुर

हिमाचल प्रदेश/Himachal Pradesh

27	Recongpeo	2003-04	'A'	CE(NZ-I), CPWD, Chandigarh	October, 2014
28	Nadaun	1996-97	'A'	CE(NZ-I), CPWD, Chandigarh	March, 2016
29	Bangana	2010-11	'A'	CE(NZ-I), CPWD, Chandigarh	February, 2016
30	Shandoi*	2016-17	B'
31	ITBP Sarhan	1994-95	'A-1'	CE(NZ-I), CPWD, Chandigarh	Oct., 2007

जम्मू एवं कश्मीर/Jammu & Kashmir

32	Badarwah	2003-04	'A-1'	CE(NZ-V), CPWD, Jammu	June, 2011
33	Samba	1979-80	B'	CE, MES, Pathankot	November, 2014
34	AFS Awantipura	1987-88	'A'	CE, MES, Udhampur	September, 2015
35	BSF Humhama ?	2010-11	'A-1'	CE(NZ-V), CPWD, Jammu	March, 2013

झारखण्ड/Jharkhand

36	Sahibganj	2010-11	'A-1'	CE, BSNL, Delhi	April, 2015
37	Lohardaga#	2017-18	'A-1'
38	Khunti#	2017-18	'A-1'
39	Dumka#	2017-18
40	Chatra#	2017-18
41	Giridih#	2017-18

केरल/Kerala

42	CRPF Peringome	2010-11	B'	CE, BSNL, Delhi	February, 2016
43	Nileswar#	2017-18

कर्नाटक/Karnataka

44	Mandya*	2015-16	'A'	CMD, HSCL, Kolkata	June, 2015
45	Udupi*	2015-16	'A'	CMD, HSCL, Kolkata	June, 2015
46	Krishnarajapuram	2011-12	'B'	CE (SZ-III), CPWD, Bangalore	Sept. 2013
47	Kadrimidri#	2017-18
48	Chennapatna#	2017-18

मध्य प्रदेश/Madhya Pradesh

49	Umaria	2010-11	'A'	CE(CZ), CPWD, Bhopal	October, 2015
50	Amba*	2016-17	'A'
51	Jamai*	2016-17	'A'
52	Pandurana*	2016-17	'A'	CE(CZ), CPWD, Bhopal	August, 2016
53	BSF Tekanpur*	2016-17	'A'
54	Chanderi #	2017-18	'A'
55	Multai #	2017-18	'A'
56	CRPF Bangrasia	2010-11	'B'	MD, UPSCIDCO, Lucknow	June, 2017
57	Ganj Basoda #	2017-18	'A'
58	No. II Neemuch #	2017-18	'A'
59	Dabra#	2017-18
60	HatLanagar#	2017-18

मणीपुर / Manipur

61	Ukhrul	2006-07	'A'	CE(NEZ), CPWD, Shillong	May, 2008
62	Leimakhong	1986-87	'A'	CE, MES, Shillong Zone	April, 2015
63	No. I Imphal	1964-65	...	CE, CPWD, Agartala	...
64	No. II Imphal	1982-83	...	CE, CPWD, Agartala	...
65	Tamenglong	2006-07

नागालैंड / Nagaland

66	Rangapahar	1992-93	A-I	CE/MES, SE FALLS, Shillong	November, 2014
----	------------	---------	-----	----------------------------	----------------

ओडिशा / Odisha

67	Hinjilicut*	2015-16	'A'	CE (EZ-V), CPWD, Bhubaneswar	August, 2016
68	Naupada	2010-11	'A'	CE (EZ-V), CPWD, Bhubaneswar	February, 2016
69	Sonepur	2010-11	'A'	CE (EZ-V), CPWD, Bhubaneswar	August, 2016
70	Kutra	2010-11	A-I	CE (EZ-V), CPWD, Bhubaneswar	August, 2016
71	Vyasnagar*	2016-17	'A'
72	Dharamgarh*	2016-17	'A'
73	Digapahandi	2010-11	'A'	CE (EZ-V), CPWD, Bhubaneswar	March, 2013
74	No. 2 Balasore*	2017-18	'A'
75	No. 3, Cuttack (NDRF Mundali)	2010-11	'A'	CE (EZ-V), CPWD, Bhubaneswar	March, 2013
76	Deogarh	2010-11	'A'	CE (EZ-V), CPWD, Bhubaneswar	December, 2017
77	No. II, Angul#	2017-18
78	Jagatsinghpur#	2017-18

पंजाब / Punjab

79	Mullanpur	1985-86	'A'	CE(WAC)Delhi Cantt.	December, 2014
80	Ubhawal	2010-11	'A'	CE(NZ-I), CPWD, Chandigarh	October, 2015
81	BSF Fazilka	2010-11	'A'	CE(NZ-V), CPWD, Jammu	Feb., 2012
82	KMS Wala	2010-11	'A'	CE(NZ-V), CPWD, Jammu	Jan., 2012
83	BSF Amarkot	2010-11	A-I'	CE(NZ-V), CPWD, Jammu	March, 2011
84	Khanpur (Roopnagar)*	2017-18	B'
85	CRPF Saraikhas	2010-11	'A'	CE(NZ-V), CPWD, Jammu	May, 2011

राजस्थान / Rajasthan

86	Dausa*	2014-15	B'	CE(NZ-III), CPWD, Jaipur	July, 2015
87	Jaisindhar*	2014-15	'A'	CE(NZ-III), CPWD, Jaipur	Sept., 2016
88	Bundi*	2014-15	B'	CE(NZ-III), CPWD, Jaipur	April, 2015
89	BSF Ramgarh	2010-11	'A'	CE(NZ-III), CPWD, Jaipur	January, 2017
90	Nagaur #	2017-18	'A'
91	CISF Jaipur#	2017-18	'A'
92	Dholpur#	2017-18
93	BSF Khajuwala	2010-11	'A I'	CE(NZ-III), CPWD, Jaipur	Oct., 2012

तमिलनाडु / Tamilnadu

94	Golden Rock*	2016-17	'B'	CE (SZ-I), CPWD, Chennai	August, 2016
95	Rameswaram	2003-04

तेलंगाना/Telangana

96	Jarasangam*	2015-16	'A'	CE (SZ-II), CPWD, Hyderabad	August, 2016
97	Bodhan*	2015-16	'A'	CMD, HSCL, Kolkata	June, 2015
98	Mancherial*	2016-17	'A'
99	Adilabad	2008-09	'A'	CE (SZ-II), CPWD, Hyderabad	Feb., 2009
100	Bhongir#	2017-18

त्रिपुरा/Tripura

101	Dhalai (Ambassa)	2006-07	'A'	CE(NEZ-II), CPWD, Agartala	September, 2015
102	CRPF Agartala	2010-11	'A'	CE(NEZ-IV), CPWD, Agartala	November, 2011

उत्तराखण्ड / Uttarakhand

103	Bageswar	2010-11	'A'	GM(N-7), C&DS, U.P Jal Nigam,	October, 2012
104	Lohaghat	2004-05	'A-I'	CE (NZ-IV), CPWD, Dehradun	October, 2008
105	Augustmuni	2004-05	A-1'	MD, UPSCIDCO, Lucknow	July, 2017
106	New Tehri Town	1986-87

उत्तर प्रदेश / Uttar Pradesh

107	MCF Rae Bareli*	2017-18
-----	-----------------	---------	-----	-----	-----

पश्चिम बंगाल / West Bengal

108	Bandel*	2017-18	'A'
109	BSF Aradhpur	2010-11	A-I'	CE(EZ-I), CPWD, Kolkata	October, 2012
110	Bolpur	2010-11	A-I'	CE(EZ-I), CPWD, Kolkata	October, 2012
111	Railway Kharagpur#	2017-18
112	BSF Krishnanagar	2010-11	'A-I'	CE(EZ-I), CPWD, Kolkata	Feb., 2012
113	Tarakeswar	2010-11	'A'	CE(WZ), APPWD, Itanagar	October, 2012

* Schools sanctioned in March 2014 (Out of 54 Nos.)

Schools sanctioned in March 2017 (Out of 50 Nos.)

? Land likely to be changed by sponsoring authorities

संजय कुमार / SANJAY KUMAR
 सहायक सचिव (फिन) / Assistant Commissioner (Fin.)
 केन्द्रीय विद्युत प्राधिकरण / Central Board of Secondary Education
 18, मीराटो रोड, इन्दौर, मध्य प्रदेश / 18, Miraato Road, Indore, Madhya Pradesh
 शहीद जगत सिंह मार्ग / Shaheed Jagat Singh Marg
 नई दिल्ली-110 016 / New Delhi-110 016

के० वि० जिनकी भूमि की पहचान कर ली गई, परन्तु के० वि० सं० के पक्ष में स्थाई अनुदान लीज अपेक्षित है / LIST OF KENDRIYA VIDYALAYAS WHERE LAND IS IDENTIFIED BUT AWAITING EXECUTION OF LEASE/ PERMANENT GRANT BASIS IN FAVOUR OF KVS as on 01-05-2018

क्र० सं०/ Sr. No	के० वि० नाम/राज्य/ Name of KV/State	विद्यालय खोलने का वर्ष / Year of opening	क्षेत्रक / Sector	क्षेत्रीय कार्यालय का नाम / Name of Region
असम / Assam				
1	RRL, Jorhat	2003-04	State Government	Guwahati
बिहार / Bihar				
2	Lakhisarai	1987-88	State Government	Patna
3	Buxar	2003-04	State Government	Patna
4	Motihari	2003-04	State Government	Patna
5	Siwan	2004-05	State Government	Patna
6	Banka	2004-05	State Government	Patna
7	Chhapra	2004-05	State Government	Patna
8	AFS, Purnia	2004-05	M.O.D (AF)	Patna
9	CRPF, Jhaphan	2010-11	Ministry H/A	Patna
10	Gopalganj	2004-05	State Government	Patna
छत्तीसगढ़ / Chhatisgarh				
11	CISF, Bhilai	2010-11	Ministry H/A	Raipur
दिल्ली / Delhi				
12	No. 4, Delhi Cantt.	1994-95	M.O.D (Army)	Delhi
13	Shakurbasti	2011-12	Ministry of Railway	Delhi
गुजरात / Gujarat				
14	AFS, Darjeepura	2010-11	M.O.D (AF)	Ahmadabad
हरियाणा / Haryana				
15	Sohna Road, Gurgaon	2003-04	M.O.D (AF)	Gurgaon
हिमाचल प्रदेश / Himachal Pradesh				
16	Alhilal	1991-92	M.O.D (Army)	Gurgaon
17	Ghumarwin	2012-13	State Government	Gurgaon
जम्मू एवं कश्मीर / Jammu & Kashmir				
18	Akhnoor No.1**	1977-78/2006-07	M.O.D (Army)	Jammu
19	Akhnoor No.2	1986-87	M.O.D (Army)	Jammu
20	Udhampur No. 2	1985-86	M.O.D (Army)	Jammu
21	Anantnag	2003-04	State Government	Jammu
22	Nubra	2003-04	State Government	Jammu
23	Jourian	2012-13	State Government	Jammu
24	BSF, Sunderbani	2010-11	Ministry H/A	Jammu

** Converted from Defence to Civil Sector vide Admn. Order dt. 29.03.2005. Again converted from Civil Sector to Defence vide Admn. Order dt. 31.07.2008

सहायक निदेशक / SANJAY K. JAR
 निदेशक / Assistant Commis-
 क्षेत्रीय विद्यालय संगठन /

झारखण्ड / Jharkhand				
25	No. 2 Dhanbad	2003-04	State Government	Ranchi
26	Surda Ghatsila	2003-04	State Government	Ranchi
27	Garhwa	2006-07	State Government	Ranchi
मध्य प्रदेश / Madhya Pradesh				
28	Kasrawad@@	2014-15	State Government	Bhopal
महाराष्ट्र / Maharashtra				
29	Yavatmal	2006-07	State Government	Jabalpur
30	CRPF, Teligaon	2010-11	Ministry H/A	Mumbai
मणीपुर / Manipur				
31	Akampet*@@	2015-16	State Government	Silchar
ओडिशा / Odisha				
32	Murgabadi	2010-11	State Government	Bhubaneswar
33	Khariar	2010-11	State Government	Raipur
34	No. 2 Cuttack	2010-11	State Government	Bhubaneswar
पंजाब / Punjab				
35	Halwara No. 2	1983-84	MOD(AF)	Chandigarh
36	Nabha Cantt.	1986-87	MOD(Army)	Chandigarh
37	BSF, Bhikiwind	2010-11	Ministry H/A	Jammu
38	No. 4 Jalandhar	1997-98	MOD(Army)	Jammu
39	Baddowal Cantt	1984-85	MOD(Army)	Chandigarh
पुदुचेरी / Puducherry				
40	Karaikal	2010-11	U.T.	Chennai
राजस्थान / Rajasthan				
41	Suratgarh No. 2\$	1997-98	MOD(AF)	Jaipur
तेलंगाना / Telangana				
42	Mahabubabad	2014-15	State Government	Hyderabad
उत्तर प्रदेश / Uttar Pradesh				
43	Chakeri No. 3	1985-86	MOD(AF)	Lucknow
44	Ghazipur	1986-87	Ministry of Finance (Opium & Alkaloid Works)	Varanasi
45	Lakhimpur	2006-07	State Government	Lucknow
46	Old Cantt. Allahabad	1989-90	MOD(Army)	Varanasi
47	Raksha Vihar, Kanpur	2003-04	MOD(Army)	Lucknow
48	CRPF, Allahabad	2014-15	Ministry H/A	Varanasi
49	Chitrakoot	2011-12	State Government	Varanasi

* Court case

उत्तराखण्ड / Uttarakhand

50	SSB, Srinagar@	1988-89/2010-11	State Government	Dehradun
----	----------------	-----------------	------------------	----------

पश्चिम बंगाल / West Bengal

51	CRPF, Durgapur	1981-82	Ministry H/A	Kolkata
52	BSF, Baikunthpur	2010-11	Ministry H/A	Guwahati
53	BSF, Raninagar	2010-11	Ministry H/A	Guwahati

@ Sponsorship changed from SSB to Civil vide Admn. I order dt. 18.06.2010 and sponsorship restored in favour of SSB with provision that land offered by State Govt. shall be accepted vide Admn. I letter dated: 10.10.2011

@@ Out of 54 KVs sanctioned in March, 2014.

\$ Proposal for meerger with KV No. 1, Suratgarh received from DC, KVS(RO) Jaipur vide letter dated: 28.08.2017. Case under examination in Admn. I.

S. No.		
1	State Government	25
2	U.T.	1
3	Ministry of Defence	16
4	Ministry of Home Affairs	9
5	Ministry of Finance	1
6	Ministry of Railway	1
	Total	53




संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त)/Assistant Commissioner (Fin.)
 केन्द्रीय वित्त सचिवालय/Kendriya Vidyapeeth Sangathan
 18, शांति क्षेत्र/18, Institutional Area
 शहीद जेठ सिंह मार्ग/Shahed Jeet Singh Marg
 नई दिल्ली-110 016/New Delhi-110 016

के० वि० जिनकी भूमि की पहचान अभी अपेक्षित है / LIST OF KENDRIYA VIDYALAYAS WHERE LAND IS YET TO BE IDENTIFIED as on 01-05-2018

क्र० सं०/ Sr. No	के० वि० नाम/ राज्य / Name of KV/State	विद्यालय खोलने का वर्ष / Year of opening	क्षेत्रक / Sector	क्षेत्रीय कार्यालय का नाम / Name of Region
बिहार / Bihar				
1	Hajipur	2003-04	State Government	Patna
2	Darbhanga	2004-05	State Government	Patna
3	Barauni	2004-05	State Government	Patna
4	Aurangabad	2010-11	State Government	Patna
5	Maharajganj	2011-12	State Government	Varanasi
जम्मू कश्मीर / Jammu & Kashmir				
6	Damana	1987-88	State Government	Jammu
7	Jindrah (*)	1986-87	M.O.D (Army)	Jammu
8	Pahalgaoon	2003-04	State Government	Jammu
9	Aminoo	2010-11	State Government	Jammu
झारखण्ड / Jharkhand				
10	HEC, Ranchi	2003-04	State Government	Ranchi
11	Gumla	2008-09	State Government	Ranchi
12	Bhurkunda	2010-11	State Government	Ranchi
केरल / Kerala				
13	Palayad	2011-12	State Government	Ernakulam
मध्य प्रदेश / Madhya Pradesh				
14	Garha	2007-08	State Government	Jabalpur
नागालैण्ड / Nagaland				
15	Zakhama (*)	1987-88	M.O.D (Army)	Tinsukia
16	CRPF, kohima	1997-98	Ministry H/A	Tinsukia
ओडिशा / Odisha				
17	Bhanjanagar	2010-11	State Government	Bhubaneswar
राजस्थान / Rajasthan				
18	Khetri Nagar	2010-11	State Government	Jaipur
19	BSF, Raisinghnagar	2010-11	Ministry H/A	Jaipur
त्रिपुरा / Tripura				
20	BSF, Taliamura	2010-11	Ministry H/A	Silchar

उत्तर प्रदेश /Uttar Pradesh				
21	IIIT, Allahabad	2003-04	State Government	Varanasi
22	Hathras	2010-11	State Government	Agra
उत्तराखण्ड /Uttarakhand				
23	No. 1, Banbasa (*)	1982-83	M.O.D (Army)	Dehradun
24	Haldwani Cantt. (*)	1989-90	M.O.D (Army)	Dehradun
25	Gwaldham	2003-04	State Government	Dehradun
26	Rishikesh	2003-04	State Government	Dehradun
27	ITBP Gauchar	1999-2000	Ministry H/A	Dehradun
(*) Sponsor does not possess land for transfer to the KV.				

S. No.		
1	State Government	19
2	U.T.	0
3	Ministry of Defence	4
4	Ministry of Home Affairs	4
5	Ministry of Railway	0
	Total	27


 संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (वित्त) / Assistant Commissioner (Fin.)
 केन्द्रीय वित्त विभाग / Central Finance Department
 18, सरदार वल्लभभाई पटेल मार्ग / Sardar Vallabhbhai Patel Marg
 शहीद जीत सिंह पार्क / Shaheed Jit Singh Park
 नई दिल्ली-110 016/New Delhi-110 016

Space norms for Kendriya Vidyalayas

Teaching/service support/administrative/class rooms


S.No	Description	No. of rooms and size required as per KVS space norms							
		A-I Type (single section from I to XII)		A-Type (two section section from I to XII)		B-Type (three section section from I to XII)		C-Type (four section section from I to XII)	
		Nos.	size in mts	Nos.	size in mts	Nos.	size in mts	Nos.	size in mts
1	Computer Lab	1	7.00 x 7.00	2	7.00 x 10.60	3	7.00 x 10.60	3	7.00 x 10.60
2	Labs	3	7.00 x 8.80 7.00 x 3.60	3	7.00 x 8.80 7.00 x 3.60	3	7.00 x 8.80 7.00 x 3.60	3	7.00 x 8.80 7.00 x 3.60
3	Jr. Sci. Lab		1	7.00 x 10.60	1	7.00 x 10.60
4	Social Sci/Geo/Resource room (Primary)	1	7.00 x 3.40	1	7.00 x 3.40	1	7.00 x 3.40	1	7.00 x 3.40
5	Social Sci/Geo/Resource room (H/Secondary)	1	7.00 x 3.40	1	7.00 x 7.00	1	7.00 x 7.00	1	7.00 x 7.00
6	Activity room	1	7.00 x 10.60	1	7.00 x 10.60	1	7.00 x 10.60	1	7.00 x 10.60
7	Art room	1	7.00 x 7.00	1	7.00 x 10.60	1	7.00 x 10.60	1	7.00 x 10.60
8	SUPW/Workshop	1	7.00 x 7.00	1	7.00 x 10.60	1	7.00 x 10.60	1	7.00 x 10.60
9	Library	1	7.00 x 10.60	1	7.00 x 14.20	1	7.00 x 17.30	1	7.00 x 21.40
10	Maths Lab	1	7.00 x 7.00	1	7.00 x 7.00	1	7.00 x 7.00	1	7.00 x 7.00
11	Principal room	1	7.00 x 7.00	1	7.00 x 7.00	1	7.00 x 7.00	1	7.00 x 7.00
12	Office	1	7.00 x 7.00	1	7.00 x 7.00	1	7.00 x 7.00	1	7.00 x 7.00
13	Staff common room	1	7.00 x 7.00	1	7.00 x 7.00	1	7.00 x 8.80	1	7.00 x 10.60
14	Vice-Principal room		1	3.40 x 3.40	1	3.40 x 3.40
15	Head Master/Head Mistress room		1	7.00 x 3.40	1	7.00 x 3.40	1	7.00 x 3.40
16	Exam. Room	1	7.00 x 3.40	1	7.00 x 3.40	1	7.00 x 3.40	1	7.00 x 3.40
17	NCC/Scout/Guide room	1	7.00 x 3.40	1	7.00 x 7.00	1	7.00 x 7.00	1	7.00 x 7.00
18	Pf.T room	1	7.00 x 3.40	1	7.00 x 7.00	1	7.00 x 7.00	1	7.00 x 7.00
19	Gen. store	1	7.00 x 3.40	1	7.00 x 7.00	1	7.00 x 7.00	1	7.00 x 7.00
20	Medical room	1	7.00 x 3.40	1	7.00 x 3.40	1	7.00 x 3.40	1	7.00 x 3.40
21	Class room	12	7.00 x 7.00	24	7.00 x 7.00	36	7.00 x 7.00	48	7.00 x 7.00

५

KV MANGALDOI (ASSAM)




KV SHIVAMOGGA (KARNATAKA)

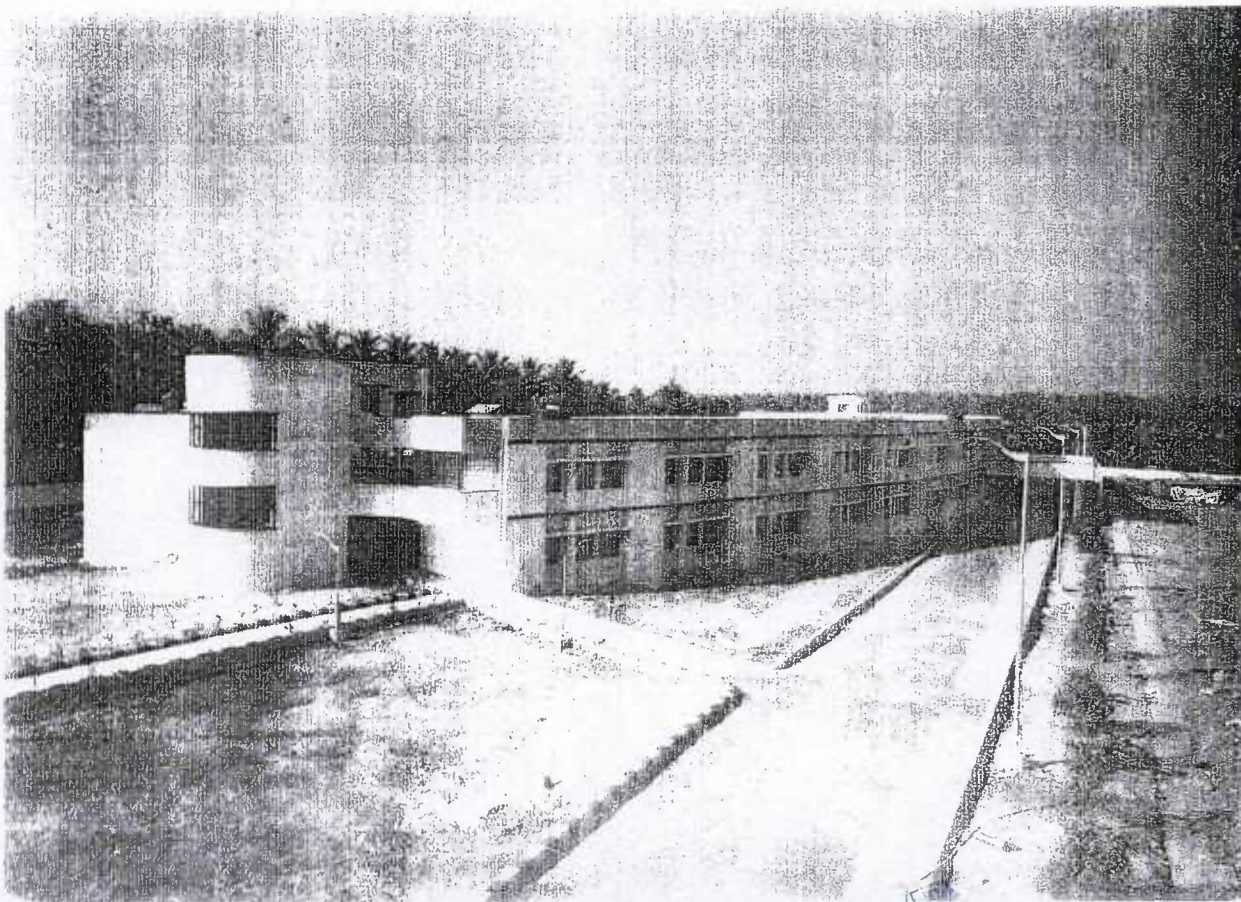

संजय कुमार / SANJAY KUMAR
 सहायक आयुक्त (विश्व) Assistant Commissioner (Field)
 राज्य विद्यालय सार्वजनिक क्षेत्र/18, Institutional Area
 शाहूद जैत सिंग मार्य
 110 016

KV REWA (M.P.)

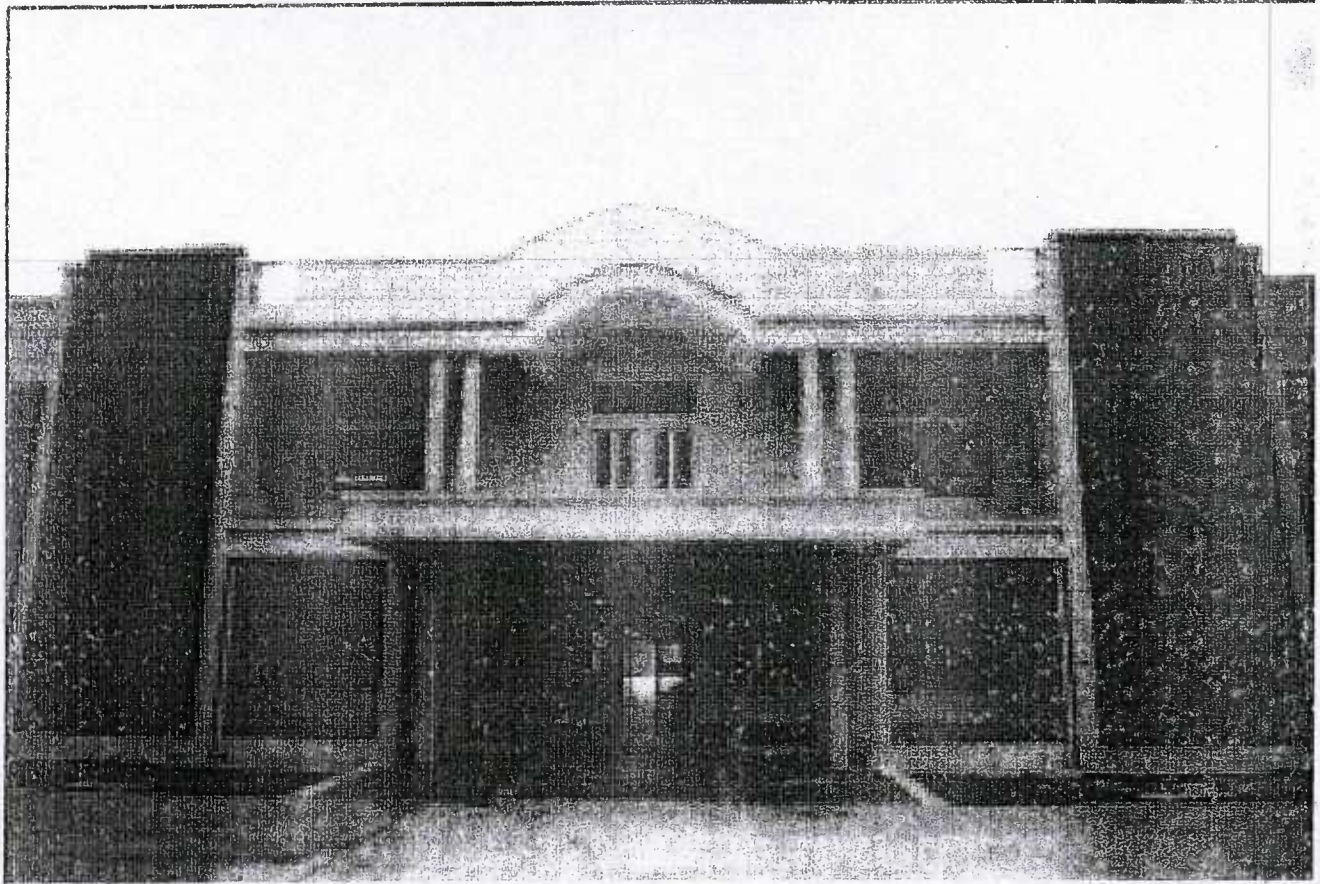

KV INDRAPURA (RAJASTHAN)





संजय कुमार / SANJAY KUMAR
म. अ. स. (वित्त) / Assistant Commissioner
क. व. विद्यापीठ, के. व. विद्यापीठ संजयपुरा
13, सरदार क्षेत्र 12, Indrapura Area
शहीद जीत सिंह मार्ग / Shaheed Jit Singh Marg
नई दिल्ली-110 016 / New Delhi-110 016

KV MOHALI (PUNJAB)



KV MADHUPUR (JHARKHAND)

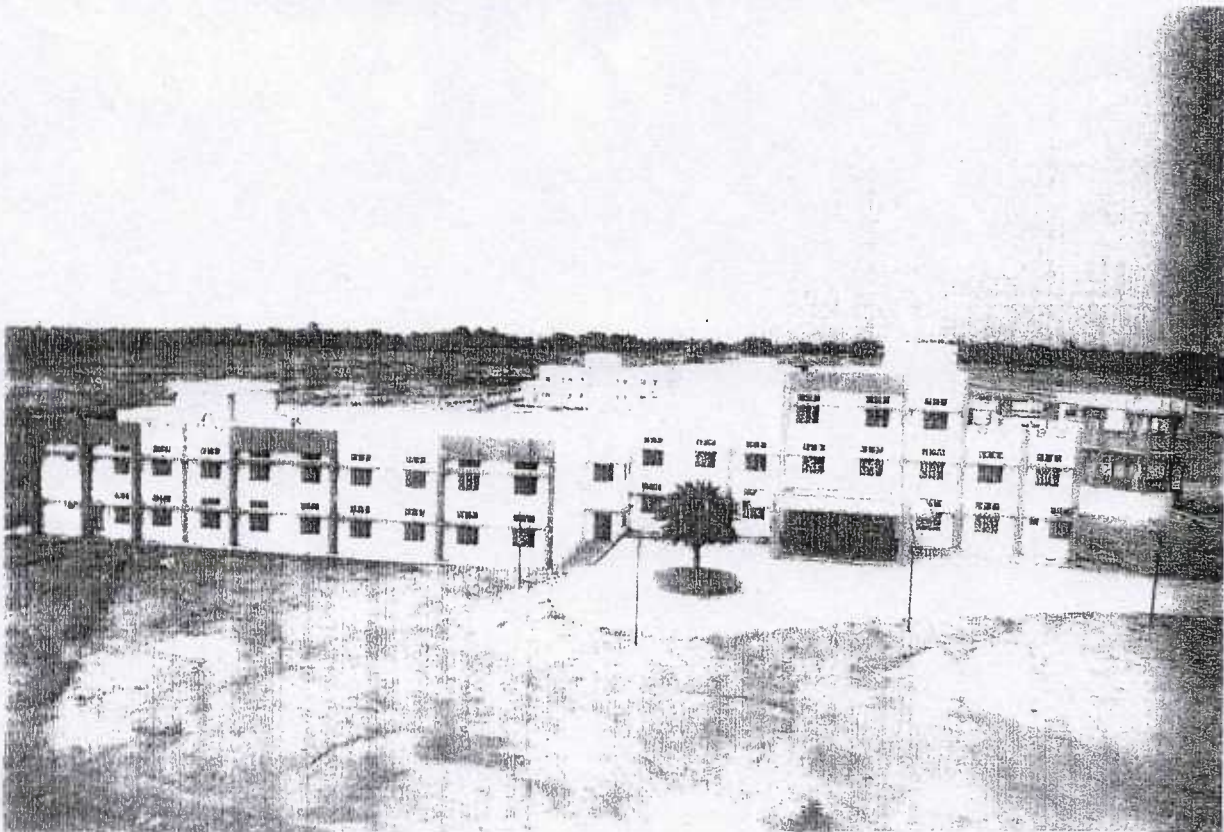


संजय कुमार / SANJAY KUMAR
सहायक आयुक्त (वित्त)/Assistant Commissioner
केन्द्रीय विद्यालय संगठन/Kendriya Vidyalaya Sangathan
18, संस्थागत क्षेत्र/18, Institutional Area
शेखर मार्ग/Shahed Jeei Sarani
110 010
